

PROJECT A: STEAM TO NATURAL GAS CONVERSION
Wednesday, July 1, 2020

Overall Status: Project is on schedule to be complete at the end of September 2020. We continue to monitor the overall schedule very closely with the contractor. The pump manufacturer has notified the contractor that due to Covid-19 they have had difficulty getting wearing bearings for their pumps and that this will delay pump deliveries to Arts, Central, West, and Plaza. The contractor is going to evaluate the impacts and issue an updated schedule as soon as they exact timing is known.

The GC, Phipps, is working diligently to have hot water on by the start of classes on August 17. Unfortunately there have been some issues with getting gas meters released and getting gas hookups to the buildings are critical to completing the project. GH Phipps, AHEC and Xcel are working through the issues. Based upon these extenuating circumstances the project will move toward hitting the August 17 date for restoring hot water to the critical areas in the affected buildings instead of providing specific dates that may change week to week due to issues or delays.

Building heat is not scheduled to be back on campus-wide until mid-September, and normally in Colorado we don't need heat until sometime in October. The contractor will have the ability to heat the buildings if we have forecasted earlier cold temperatures. Heat may be on at the earlier dates shown, but the entire system will be going through commissioning and testing through mid-Sept.

Xcel work to install gas lines is complete except for hardscape repairs. Hardscape repairs have been completed except in front of the Science Building, which will happen sometime in late July due to Phipps being in the area with other work now.

Note: There will be no work going on Friday, July 3 through the weekend in celebration of the 4th of July.

Happening next week, by Building:

Tivoli Commons:

- After further investigation and additional excavation it turns out Xcel did bore through a campus irrigation mainline near the Quad. Repairs are underway.

Boulder Creek:

A. Next Week:

- Continue installation of Boilers, piping and equipment in the Penthouse Mechanical Room.

B. Upcoming:

- Gas line installation.

No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 18	May 18	June 2	August 17	August 31*	Sept. 20

***Heating will be possible, but commissioning and testing will go on through September.**

C. Impacts:

- Contractors are to utilize scaffold stair tower on north side of building.
- No heat and no hot water in building as noted above.
- Xcel has pulled the gas meter so there is no gas to the building through late July.

Plaza:

A. Next week:

- Continued installation of boilers and associated equipment.
- Start work on interior landing from Penthouse to 3rd Floor (work will go through mid-August)
- Ongoing finishes on interior walls in Boiler Room.
- Monday, June 29: Began repairs to water damaged office 220; starting with drywall and then moving to the ceiling; work will continue through July.
- Install the ceiling grid in the Level 3 corridor as shown below.

B. Upcoming:

- New gas meter from Xcel – date up in the air; awaiting Xcel meter release.


No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 13	May 13	June 10	August 17	August 31*	Sept. 18

***Heating will be possible, but commissioning and testing will go on through September.**

Note: Plaza Health Center has electric hot water heaters and will not experience a hot water outage.

C. Impacts:

- Contractors are to utilize scaffold stair tower on east side of building for Boiler Penthouse work.
- No heat and no hot water as noted above.
- Anticipate a Thursday, July 16 and Friday, July 17 electrical shut-down that will effect 3rd floor HVAC, outlets and lights, including all 3rd floor classrooms and office. NOTE: We believe that the AC can remain running via manual operation of the system during this period. If this changes we will issue an update.

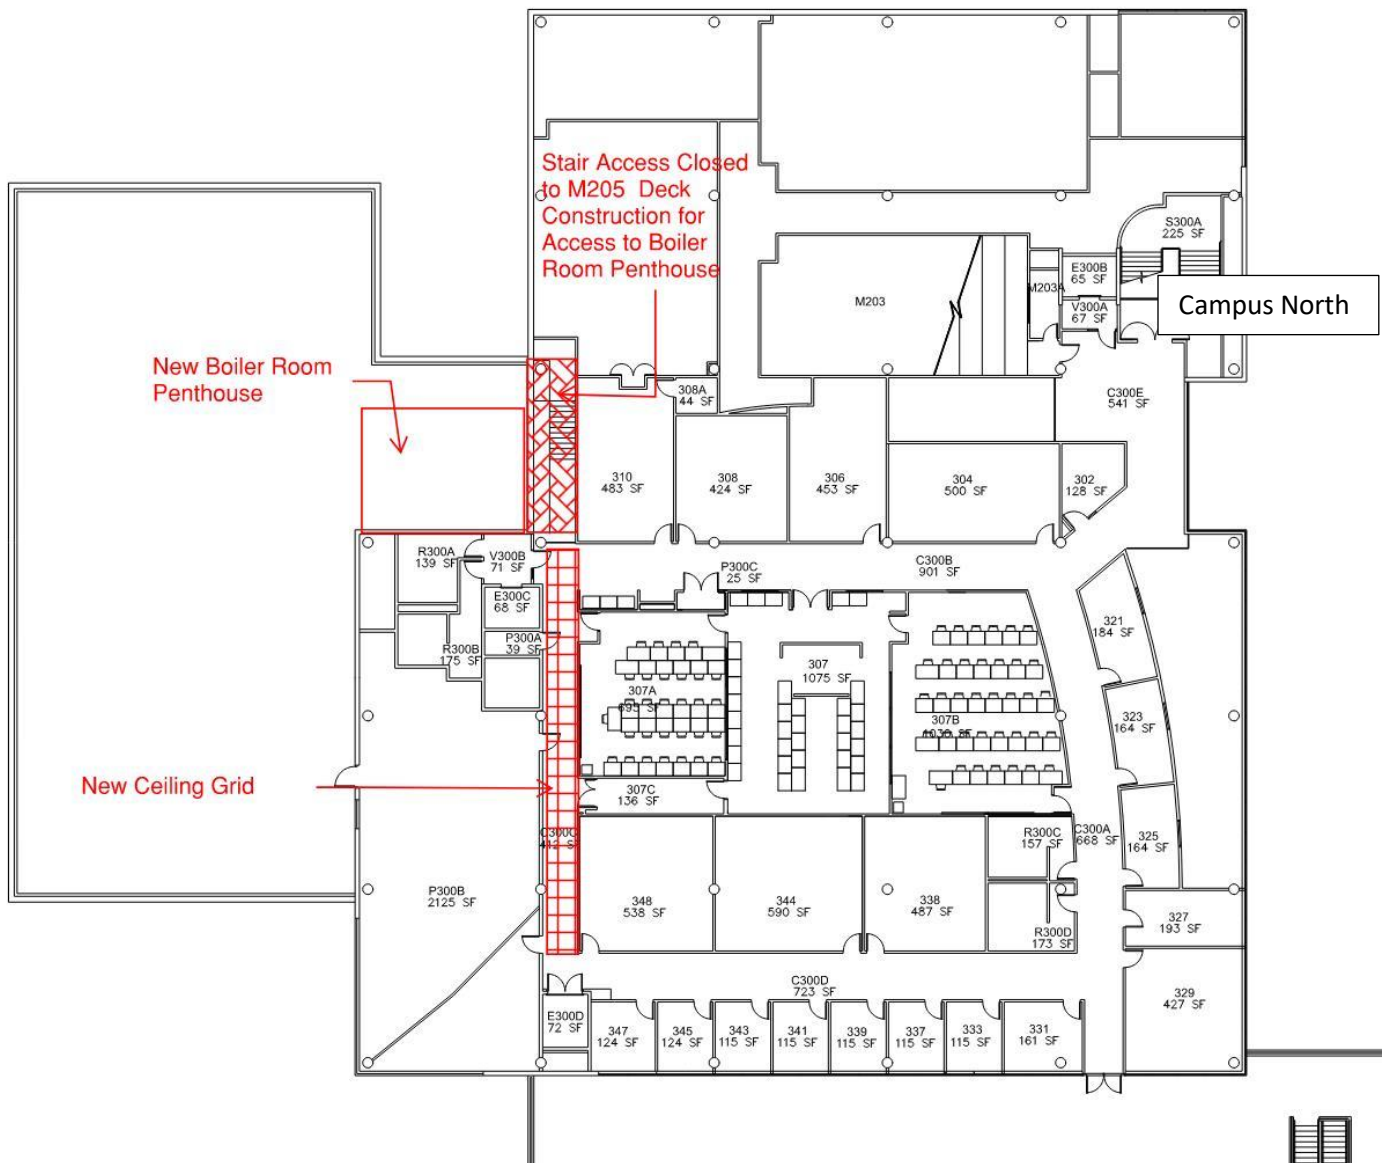

PE:

A. Next week:

- Continue installation of Boilers, piping and equipment in the Penthouse Mechanical Room.
- Gas outage continues
- New gas meter from Xcel – date up in the air; awaiting Xcel meter release.
- Ongoing finishes on interior walls in Boiler Room

B. Upcoming:

- Continued work on the boiler room/penthouse
- Boiler installation work continues
- Whole building electrical outages Tuesday, July 7 from 6 am to 9 am and on Friday, July 10 from 3 pm – 6 pm. There will be no HVAC during this entire period.

- Permanent repairs to PE 215 and 209 will be accomplished after the roof has been permanently been patched and dried in, starting approximately July 9.

No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 12	May 7	June 10	August 17	August 31 *	Sep. 17

***Heating will be possible, but commissioning and testing will go on through September.**

C. Impacts:

- Natural gas has been shut down to the building. (If hot water is needed during this period, there is a work around that can be done if necessary.)
- Contractors are to utilize scaffold stair tower on south side of building for Boiler Penthouse work.

Arts:

A. Next week:

- Continue installation of Boilers, piping and equipment in the Mechanical Room.
- Install flues in lobby and at hallway to exterior.
- Relocate fire sprinkler lines in north lobby area.
- Begin installing ceiling grid in the hallway.
- Barriers and signage will go up at the Northeast entry of Arts, directing people where to enter/exit the building.

B. Upcoming:


- Brick patching will start at exterior the week of July 6 of July 13.
- Ceiling work in the 1st floor northeast lobby will start go through early August.

No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 18	May 18	June 10	August 17	August 31*	Sept. 11

***Heating will be possible, but commissioning and testing will go on through September.**

C. Impacts:

- No heat and no hot water as noted above.
- Majority of work is concentrated in the northeast corner of the building.
- No gas to Arts Kiln Room

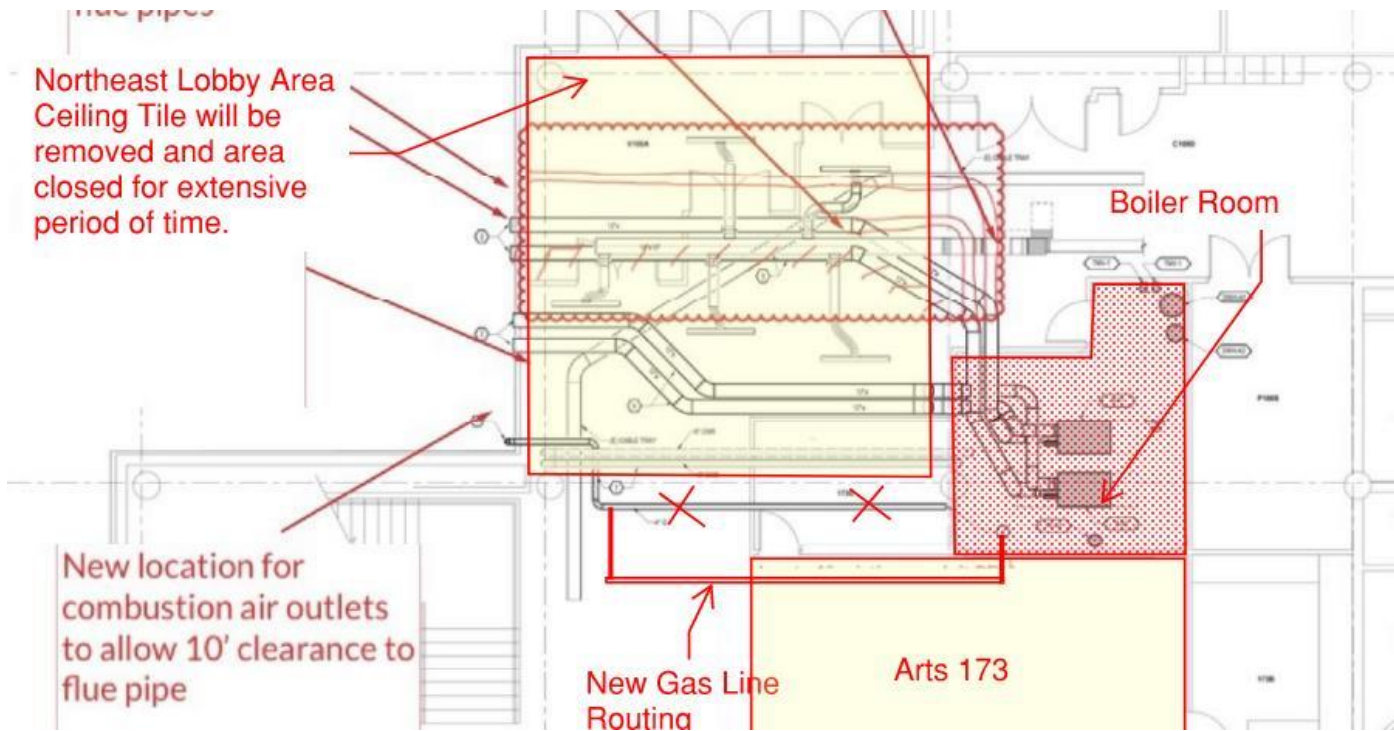

Central Classroom:

- A. Next week:
 - o Continue installation of Boilers, piping and equipment in the Mechanical Room.
 - o Install flues thru Central Alley wall.
 - o Continued installation insulation in south wall of Central Classroom 101

- B. Upcoming:
 - o Install framing for exterior wall.
 - o Begin MEP rough-ins
 - o Whole building electrical outage, 30 minute duration, Tuesday, July 14; being coordinated with Metro IT.

No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 18	May 18	June 10	August 17	August 31*	Sep. 14

***Heating will be possible, but commissioning and testing will go on through September.**

- C. Impacts:
 - o No heat and no hot water as noted above.

West Classroom:

- A. Next week:
 - o Continue installation of Boilers, piping and equipment in the Mechanical Room.
 - o Installation of gas line from mechanical room to roof (thru August)
 - o Pipe chase/shaft being built from first floor to roof (thru August)
 - o Paint Mechanical Room

B. Upcoming:

- o Air Handler shut down dates TBD

No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 26	May 26	June 10	August 17	August 31*	Sept. 21

***Heating will be possible, but commissioning and testing will go on through September.**

C. Impacts:

- o Noisy for core drilling on roof.
- o No heat and no hot water as noted above.
 - o WC 243 Closet conversion into flue chase thru August 7 (confirmed with Saima Reece and coordinated where any returning employees can work during this installation)
 - o 1st Floor office 026B - ongoing above ceiling work thru August 7
 - o 2nd floor hall next to office 241B - on going above ceiling work thru August 7

Cherry Creek:

A. Next week:

- o Install gas line thru east entry lobby thru July 24.
- o Air handler shut down affects 3rd Floor to move Pneumatic Controls compressor
- o Build new partitions at Mechanical Room
- o Boilers arrive week of July 6.
- o Begin installation of ceiling grid on 1st floor.

B. Upcoming:


- o Mid-July shut down of air handling units – dates will coincide with electrical outage and continue through Friday, July 24.
- o Full Building electrical outage on Tuesday, July 21 from 6 am to 9 am and Wednesday, July 23 from noon to 3 pm; NO HVAC this week.

No Steam / No Heat	No Hot Water	Boiler Delivery	Hot Water Returns	Heating Sys Active	Building Complete
May 19	May 19	June 29	August 17	August 31*	Sept. 29

***Heating will be possible, but commissioning and testing will go on through September.**

C. Impacts:

- o No heat and no hot water as noted above.
- o Gas piping will run from the east side of the building into the center of the building and up from the first floor to the third floor. As a result there will be some work in the main lobby area on the east side of the building.
- o No AC and electric as noted above

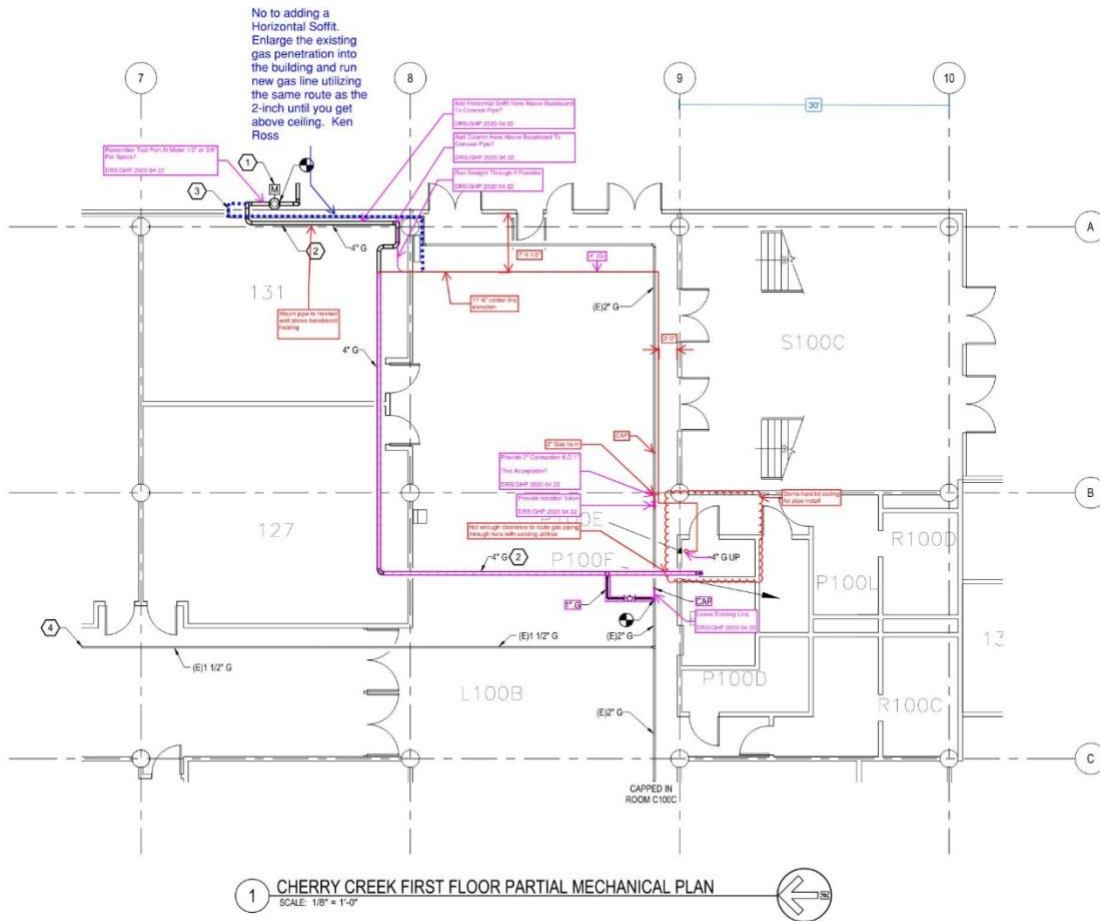

Science:

A. This week:


- Exterior trenching between wings of building continues; Will effect ingress/egress from the north to the main atrium butterfly area. Way finding signage showing entry/exits and barriers will be installed at doors and hallways.
- West wing north hallway corridor piping complete; build back of hallway underway.
- Roof penetrations and curb installations above 1067 Projection Booth completed this week; flues to be installed over next 2 weeks.
- Continued installation of Boilers, piping and equipment in the Mechanical Room.
- Frame and patch flue opening in exterior walls
- Install exterior stairs for additional exit out of Mechanical room.
- Install the ceiling grid in the corridor shown below.

B. Upcoming:

- Installation of grid ceiling on 1st floor.
- Drywall/ceiling patching at 1st floor gender neutral restrooms.
- Beginning planning and coordination of basement work relating to Vivarium and washing cage.

No Steam / No Heat	No Hot Water	Boiler Delivery		Hot Water Returns	Heating Sys Active	Building Complete
June 4	May 26	June 10		August 17	August 31*	Sept. 29
<p>Note: Vivarium 180 degree water need will NOT be affected one heat exchanger will be intact and not be removed until boilers are operational.</p>						

*Heating will be possible, but commissioning and testing will go on through September.

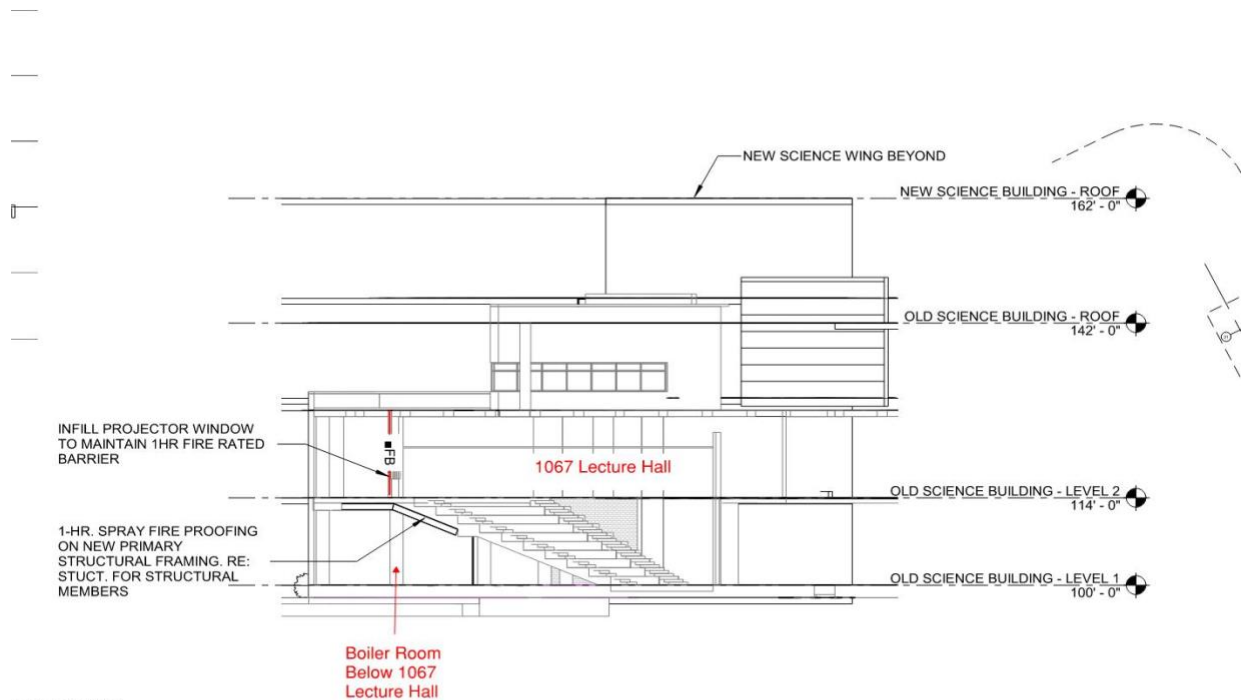

BUILDING -
EQUIPMENT
EL 01


5 CODE COMPLIANCE SECTION
1/16" = 1'-0"

ROOM - 1067A / A06:
PROJECTION RM / P
SCOPE:
CONVERT PROJECT
MECHANICAL SUEP


C. Impacts:


- The Science air handling unit has been shut down that provides tempered air to the 1067 Lecture Hall.
- No heat and no hot water as noted above.
- North corridor of Old Science will be under construction to allow pipe installation until August 7.
- Hot water piping from Old Science to New Science will cause the main entrance on the north side of the building to be closed thru approximately August 14.
- Two Gender Neutral Restrooms on 1st Floor are now off line until August 7.
- Lots and lots of noisy work outside and surrounding the projection booth.


SCIENCE PUBLIC SAFETY BARRIER AND WAYFINDING PLAN 7-6 TO 8-14


 = AREA NOT ACCESSIBLE TO PUBLIC 7-6 TO 8-14

 = 4' SAFETY PANEL BARRIER WITH SIGN "HALLWAY CLOSED - DETOUR" WITH DIRECTIONAL ARROW

 = 6' CHAIN LINK FENCE WITH EMERGENCY EGRESS SIGNAGE AND ARROWS AS NEEDED

 = PUBLIC ACCESS ROUTE

 = EMERGENCY EXIT ROUTE (OPEN TO PUBLIC ONLY IN EMERGENCIES)


 = REMOVABLE BARRIER W/ SIGN "IN CASE OF EMERGENCY - REMOVE BARRIER"

SIGNAGE ON FENCE

ENTRANCE DETOUR


SIGNAGE PLACED ON REMOVABLE PANEL

ENTRANCE CLOSED PLEASE USE WEST ENTRANCE

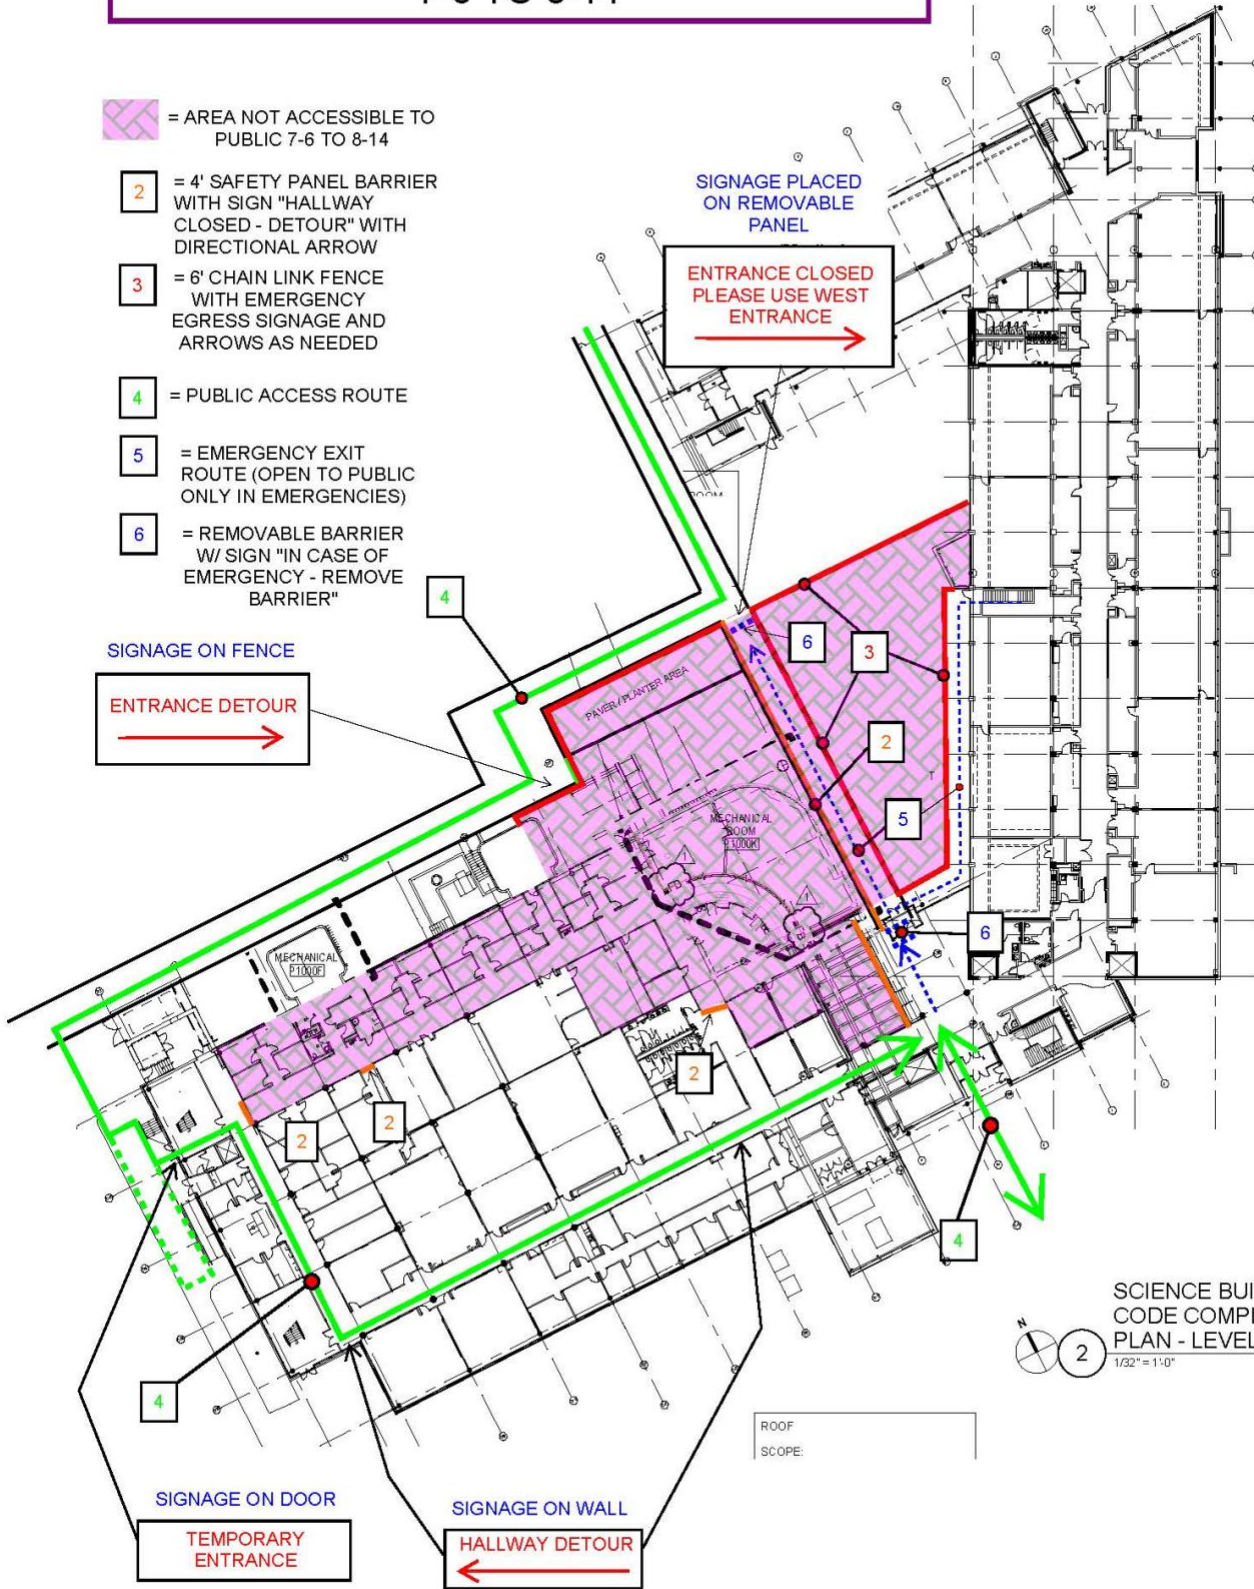INFILL PROJECT TO MAINTAIN BARRIER

1-HR. SPRAY F ON NEW PRIM STRUCT. FOR S MEMBERS


SCIENCE BUILDING -
CODE COMPLIANCE
PLAN - LEVEL 01



ROOF SCOPE:

SIGNAGE ON DOOR
TEMPORARY ENTRANCE

SIGNAGE ON WALL
HALLWAY DETOUR

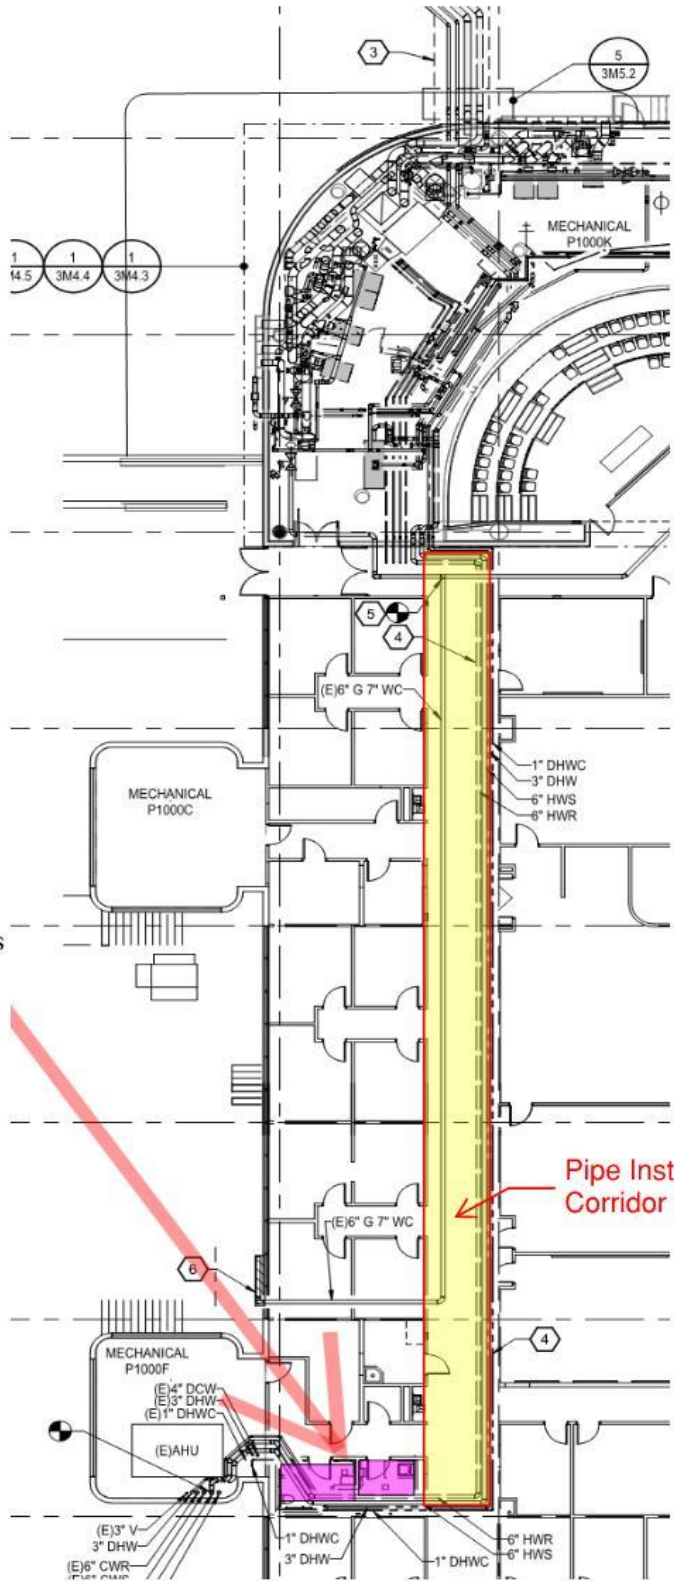Gender Neutral Restrooms

Pipe Installation in
Corridor Ceiling
